


0180	Building Substantial Completion	1	15APR19	15APR19
0210	Punchlist	15	16APR19	07MAY19
1030	Site Substantial Completion	1	29APR19	29APR19
0190	Close - Out Documentation	30	04JUN19	15JUL19
0200	Final Completion	1	16JUL19	16JUL19
Construction				
2520	Building Excavation (BY	1	13APR18	04MAY18
0120	CIPC - Basement Footings	8	02MAY18	07JUN18
0130	CIPC - Basement Foundation	15	17MAY18	20JUN18
0540	CIPC - Elevator Pit	3	08JUN18	12JUN18
1100	Plumbing Underground -	8	08JUN18	19JUN18
2710	CIPC - Basement Slab on	2	20JUN18	21JUN18
1120	Plumbing Rough In - Basement	10	22JUN18	06JUL18
1470	Detention Frames	3	27JUN18	29JUN18
1280	Basement Waterproofing	12	07MAY18	03JUL18
0550	CIPC - Footings	10	21JUN18	05JUL18
1330	Masonry Elevator Shaft	7	21JUN18	29JUN18
0560	CIPC - Frost Walls	10	06JUL18	19JUL18
1110	Foundation Drain Tile	6	05JUL18	12JUL18
2530	Foundation Backfill (BY	1	13JUL18	13JUL18
0600	CIPC - Exterior Planters	10	16JUL18	27JUL18
1890	Site Concrete - Emergency	4	16JUL18	19JUL18
1870	Com Ed Service Rough IN	3	20JUL18	24JUL18
1300	Masonry Bearing Walls CL A t	15	01AUG18	21AUG18
2790	Plumbing Underground North of	5	20JUL18	26JUL18
1850	Site Electrical / Lighting Rough	7	20JUL18	30JUL18
2800	Slab on Grade - North of CL 3.4	2	27JUL18	30JUL18
2810	Masonry Bearing CL 3.4 - 2 /	10	31JUL18	13AUG18
0760	Structural Steel Erection - East	10	02JUL18	16JUL18
0610	CIPC - Structural Slab	7	22AUG18	30AUG18
1040	Structural Steel Erection - West	4	31AUG18	06SEP18
0770	Structural Steel Detailing - East	20	17JUL18	13AUG18
2660	Structural Steel Detailing -	4	07SEP18	12SEP18
2740	Metal Roof Decking - West of	3	13SEP18	17SEP18
0780	Metal Floor Decking	5	14AUG18	20AUG18
0620	CIPC - Slab on Metal Deck -	3	21AUG18	23AUG18
1910	Electrical Rough IN Basement	20	21AUG18	18SEP18
1550	Light Gauge Roof Truss	15	21AUG18	11SEP18
1980	Electrical Rough IN 1st FL	25	24AUG18	28SEP18
1140	Plumbing Rough IN - 1st FL	14	24AUG18	13SEP18
0790	Metal Roof Decking	8	12SEP18	21SEP18
1920	Electrical Rough In Basement -	15	19SEP18	09OCT18
0630	CIPC - Slab on Metal Deck -	3	24SEP18	26SEP18
2750	Low Roof Concrete Infill & Curb	3	24SEP18	26SEP18
2690	Plumbing Underground - On	10	24SEP18	05OCT18
1180	Roof Related Wood Blocking	9	24SEP18	04OCT18
2000	Electrical Rough IN - 2nd FL	16	27SEP18	18OCT18
2470	Exterior Metal Stud Wall	6	27SEP18	04OCT18
1150	Plumbing Rough IN - 2nd Fl	7	27SEP18	05OCT18
1160	Plumbing Rough IN - Roof	5	27SEP18	03OCT18
1990	Electrical Rough IN - 1st FL	15	01OCT18	19OCT18
1500	Asphalt Shingle Roofing	14	05OCT18	24OCT18
2490	Exterior Metal Stud Wall	10	05OCT18	18OCT18
1510	Membrane Roofing Assembly	10	05OCT18	18OCT18
2700	CIPC - Slab on Grade	5	08OCT18	12OCT18
1200	Hollow Metal Frame Installation	10	15OCT18	26OCT18
2260	Metal Stud Framing - 1st FL	15	15OCT18	02NOV18
2270	Metal Stud Framing - 2nd FL	10	15OCT18	26OCT18
2250	Metal Stud Framing - Basement	8	15OCT18	24OCT18
0800	Misc. Metals - Metal Stair	15	15OCT18	02NOV18
0730	Polished Concrete Flooring -	5	15OCT18	19OCT18

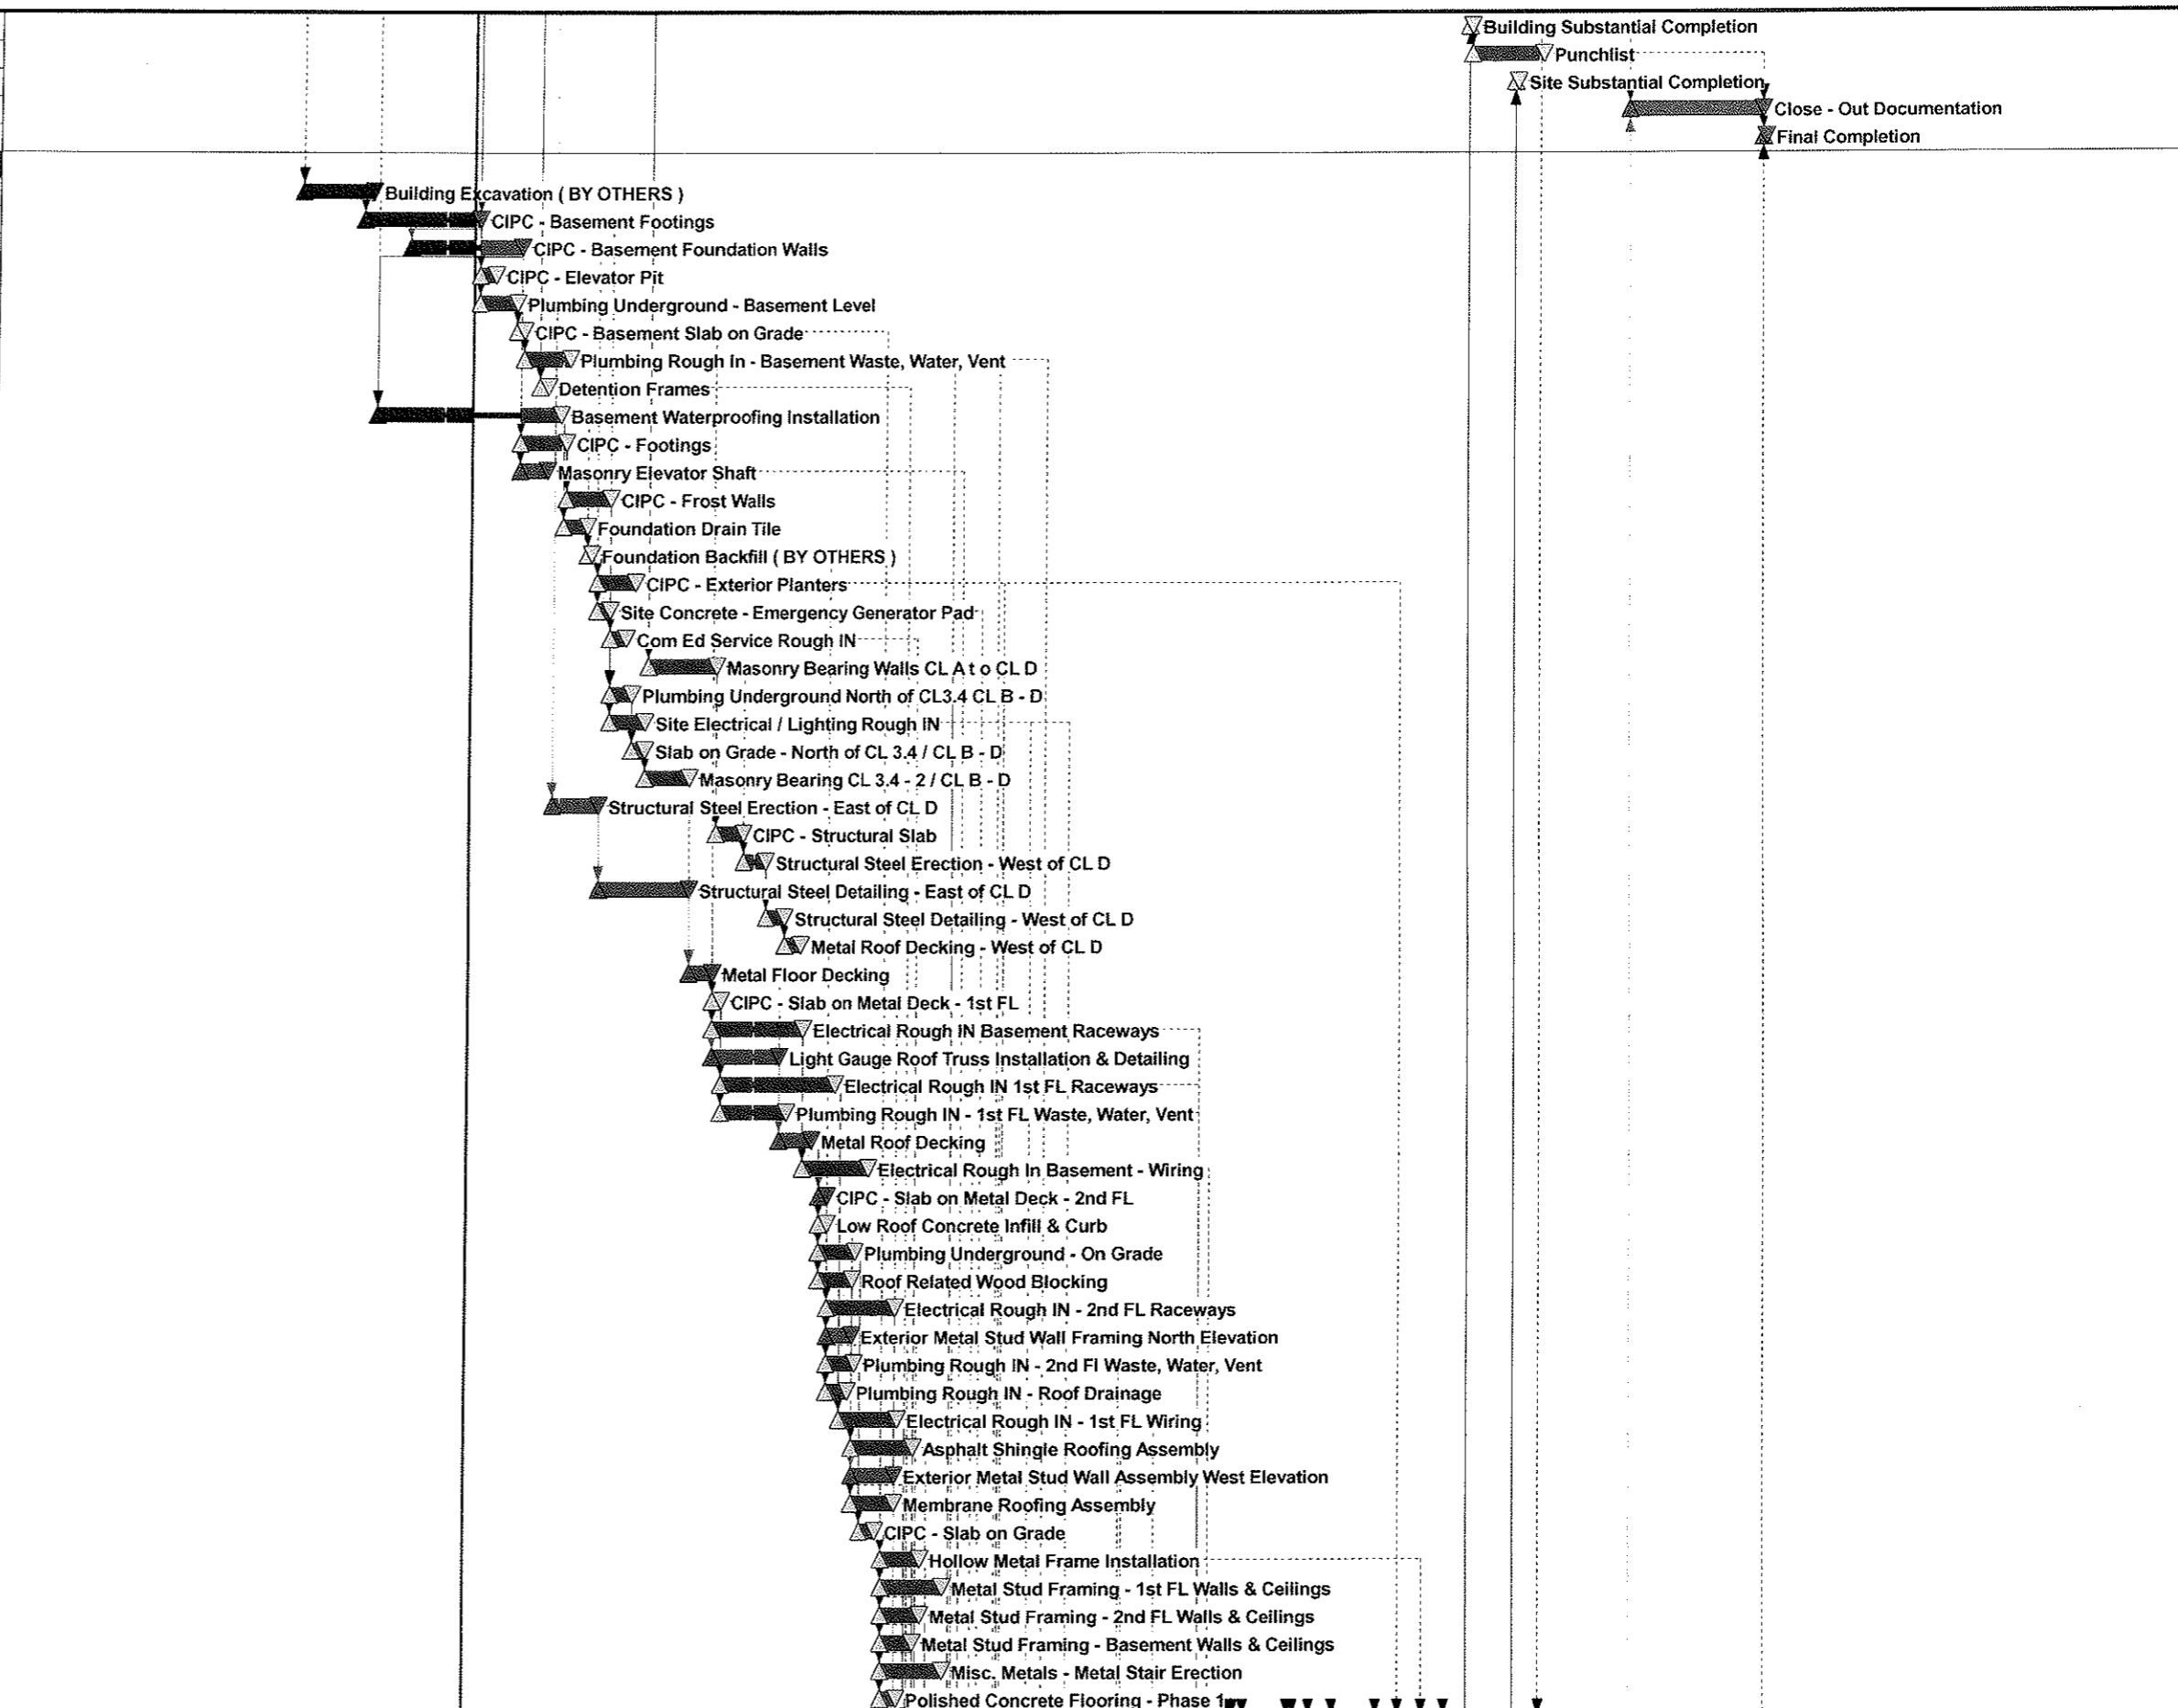

Project Start	08JAN18	▲	▲	▼	Early Bar
Project Finish	16JUL19	▲	▲	▼	Progress Bar
Data Date	06JUN18	▲	▲	▼	Critical Activity
Run Date	06JUN18	▲	▲	▼	

CMCP

City of Countryside
New Municipal Complex
Updated 6/06/2018

Sheet 2 of 5




2180	CCTV System Rough IN -	7	19OCT18	29OCT18
2160	Detention Security System	10	19OCT18	01NOV18
2010	Electrical Rough IN - 2nd FL	12	19OCT18	05NOV18
2480	Exterior Metal Stud Wall	5	19OCT18	25OCT18
1750	HVAC Rooftop Mechanical	5	19OCT18	25OCT18
1740	HVAC Rough IN - Basement	15	19OCT18	08NOV18
1060	Sallyport Sectional Overhead	8	19OCT18	30OCT18
1580	Skylight Installation	2	19OCT18	22OCT18
2040	Electrical Trim - 1st FL MEP	9	22OCT18	01NOV18
1610	Interior Non Load Bearing	10	22OCT18	02NOV18
1290	Air Barrier Installation -	10	23OCT18	05NOV18
1320	Masonry Veneer - North	20	23OCT18	19NOV18
1590	Masonry Veneer - West	16	23OCT18	13NOV18
2770	Building Electrical Service Trim	7	25OCT18	02NOV18
1490	Fire Protection Riser / Fire	3	25OCT18	29OCT18
1700	HVAC Sheet Metal Rough IN -	15	25OCT18	14NOV18
1720	HVAC Sheet Metal Rough IN -	10	25OCT18	07NOV18
1680	HVAC Sheet Metal Rough IN -	12	25OCT18	09NOV18
1010	Operable Partition Installation -	1	25OCT18	25OCT18
2500	Exterior Metal Stud Wall East	7	26OCT18	05NOV18
1190	In Wall Blocking	6	26OCT18	02NOV18
1600	Masonry Veneer - South	12	26OCT18	12NOV18
1560	Spray Applied Fire-Proofing	3	29OCT18	31OCT18
1710	HVAC Piping Rough IN - 1st FL	15	01NOV18	21NOV18
1730	HVAC Piping Rough IN - 2nd	10	01NOV18	14NOV18
1690	HVAC Piping Rough In -	10	01NOV18	14NOV18
2170	Detention Security System -	10	02NOV18	15NOV18
2280	Basement Gypsum Board	12	05NOV18	20NOV18
1940	Electrical Trim - Elevator Power	3	05NOV18	07NOV18
1760	HVAC - BAS System Raceways	15	05NOV18	26NOV18
0810	Misc. Metal - Stair Railings	10	05NOV18	16NOV18
2200	Electrical Trim - Rooftop	3	06NOV18	08NOV18
1570	Foamed In Place Insulation	10	06NOV18	19NOV18
1310	Masonry Veneer - East	11	06NOV18	20NOV18
2240	Metal Stud Framing / Sheating -	15	06NOV18	27NOV18
1840	Electric Traction Elevator	16	08NOV18	30NOV18
2090	Electrical Trim- 2nd FL MEP	5	08NOV18	14NOV18
1960	Electrical Trim - Basement	5	12NOV18	16NOV18
2420	South Elevation -1st FL	8	13NOV18	23NOV18
1880	Emergency Generator	7	14NOV18	23NOV18
2400	West Elevation - 1st FL	7	14NOV18	23NOV18
1480	Plumbing Equipment Trim	4	19NOV18	23NOV18
2290	1st FL Gypsum Board	20	20NOV18	18DEC18
2300	2nd FL Gypsum Board	14	20NOV18	10DEC18
1540	EIFS Installation	20	20NOV18	18DEC18
2390	North Elevation - Window	8	20NOV18	30NOV18
2760	Basement Porcelain Floor &	8	21NOV18	03DEC18
2370	East Elevation - 1st FL Window	15	21NOV18	12DEC18
0580	Site Concrete - Curbs	5	21NOV18	28NOV18
0570	Site Concrete - Fence	4	21NOV18	27NOV18
0640	Site Concrete - Monument	10	21NOV18	05DEC18
0590	Site Concrete - Walks, Aprons	15	21NOV18	12DEC18
0920	Fire Protection - Clean Agent	3	23NOV18	27NOV18
0900	Fire Protection Rough IN / Trim	15	23NOV18	13DEC18
1340	Masonry Elevator Shaft - Door	3	23NOV18	27NOV18
1830	Plumbing Equipment - Start	2	26NOV18	27NOV18
1380	Site Masonry - Masonry Screen	3	26NOV18	28NOV18
1770	HVAC BAS Systems - Wiring	15	27NOV18	17DEC18
1530	DEFS Installation	20	28NOV18	27DEC18
1050	Fire Protection - Clean Agent	5	28NOV18	04DEC18

▼	CCTV System Rough IN - Wiring
▼	Detention Security System Rough IN - Wiring
▼	Electrical Rough IN - 2nd FL Wiring
▼	Exterior Metal Stud Wall Assembly South Elevation
▼	HVAC Rooftop Mechanical Equipment
▼	HVAC Rough IN - Basement Mechanical Equipment
▼	Sallyport Sectional Overhead Doors
▼	Skylight Installation
▼	Electrical Trim - 1st FL MEP Equipment
▼	Interior Non Load Bearing Masonry Partitions
▼	Air Barrier Installation -
▼	Masonry Veneer - North Elevation
▼	Masonry Veneer - West Elevation
▼	Building Electrical Service Trim
▼	Fire Protection Riser / Fire Pump Installation
▼	HVAC Sheet Metal Rough IN - 1st FL
▼	HVAC Sheet Metal Rough IN - 2nd FL
▼	HVAC Sheet Metal Rough IN - Basement
▼	Operable Partition Installation - Phase 1
▼	Exterior Metal Stud Wall East Elevation
▼	In Wall Blocking
▼	Masonry Veneer - South Elevation
▼	Spray Applied Fire-Proofing
▼	HVAC Piping Rough IN - 1st FL
▼	HVAC Piping Rough IN - 2nd FL
▼	HVAC Piping Rough In - Basement
▼	Detention Security System - Trim
▼	Basement Gypsum Board Installation Tape & Finish
▼	Electrical Trim - Elevator Power
▼	HVAC - BAS System Raceways
▼	Misc. Metal - Stair Railings
▼	Electrical Trim - Rooftop Mechanical Equipment
▼	Foamed In Place Insulation
▼	Masonry Veneer - East Elevation
▼	Metal Stud Framing / Sheating - Soffits & Fascia
▼	Electric Traction Elevator Installation
▼	Electrical Trim- 2nd FL MEP Equipment
▼	Electrical Trim - Basement MEP Equipment
▼	South Elevation -1st FL Window Framing & Glazing
▼	Emergency Generator Installation
▼	West Elevation - 1st FL Window Framing & Glazing
▼	Plumbing Equipment Trim
▼	1st FL Gypsum Board Installation Tape & Finish
▼	2nd FL Gypsum Board Installation Tape & Finish
▼	EIFS Installation
▼	North Elevation - Window Framing & Glazing
▼	Basement Porcelain Floor & Wall Tile
▼	East Elevation - 1st FL Window Framing & Glazing
▼	Site Concrete - Curbs
▼	Site Concrete - Fence Foundations
▼	Site Concrete - Monument Footings/Plaza Walls
▼	Site Concrete - Walks, Aprons & Paving
▼	Fire Protection - Clean Agent System Rough IN
▼	Fire Protection Rough IN / Trim Exposed Areas
▼	Masonry Elevator Shaft - Door Frame Infills
▼	Plumbing Equipment - Start Up/Functional Testing
▼	Site Masonry - Masonry Screen Walls
▼	HVAC BAS Systems - Wiring
▼	DEFS Installation
▼	Fire Protection - Clean Agent System Trim


Project Start	08JAN18	▼	Early Bar
Project Finish	16JUL19	▶	Progress Bar
Data Date	06JUN18	▶	Critical Activity
Run Date	06JUN18		

CMCP

City of Countryside
New Municipal Complex
Updated 6/06/2018



0870	2nd FL Resilient Flooring	10	01FEB19	14FEB19
1670	2nd FL Terrazzo	15	01FEB19	21FEB19
0740	Polished Concrete Flooring -	7	01FEB19	11FEB19
0750	1st FL Terrazzo Flooring	20	04FEB19	01MAR19
1440	Acoustical Ceiling Tile - 1st FL	10	04FEB19	15FEB19
2210	Electrical Systems Start Up	5	04FEB19	08FEB19
1790	HVAC - BAS System -	10	04FEB19	15FEB19
1260	Plastic Paneling Installation	2	04FEB19	05FEB19
2330	Porcelain Tile Flooring - 2nd FL	8	04FEB19	13FEB19
1220	Toilet Partition Installation	8	04FEB19	13FEB19
2780	Basement Resilient Flooring	7	05FEB19	13FEB19
1250	Building Expansion Joint	3	12FEB19	14FEB19
1020	Operable Partition Installation -	3	14FEB19	18FEB19
1230	Toilet Accessory Installation	5	14FEB19	20FEB19
1800	HVAC Start - UP	5	18FEB19	22FEB19
1070	Interior Coiling Doors	4	18FEB19	21FEB19
2350	Window Treatment / Shade	5	18FEB19	22FEB19
0720	Resinous Flooring / Carpeting &	15	20FEB19	12MAR19
1640	Council Chambers Wood	15	25FEB19	15MAR19
1820	HVAC System - Test & Balance	5	25FEB19	01MAR19
1630	Corridor Wood Paneling &	20	04MAR19	29MAR19
2440	Aluminum Entrance Doors	5	04MAR19	08MAR19
1650	Lobby Wood Paneling & Trim	15	04MAR19	22MAR19
1270	FEC Installation	2	13MAR19	14MAR19
0860	1st FL Resilient Flooring	10	18MAR19	29MAR19
2220	Interior Lettering/ Signage	3	25MAR19	27MAR19
0680	Landscape Plantings	10	25MAR19	05APR19
1210	Door & Hardware Installation	10	01APR19	12APR19
1240	Entrance Mat Installation	3	01APR19	03APR19
0690	Landscape - Turfs & Grasses	10	08APR19	19APR19
2230	Building Flush Out	15	15APR19	03MAY19
0660	Asphalt Paving - Surface	2	22APR19	23APR19
0700	Landscape Furnishings	5	22APR19	26APR19
1810	Functional Testing &	20	07MAY19	03JUN19

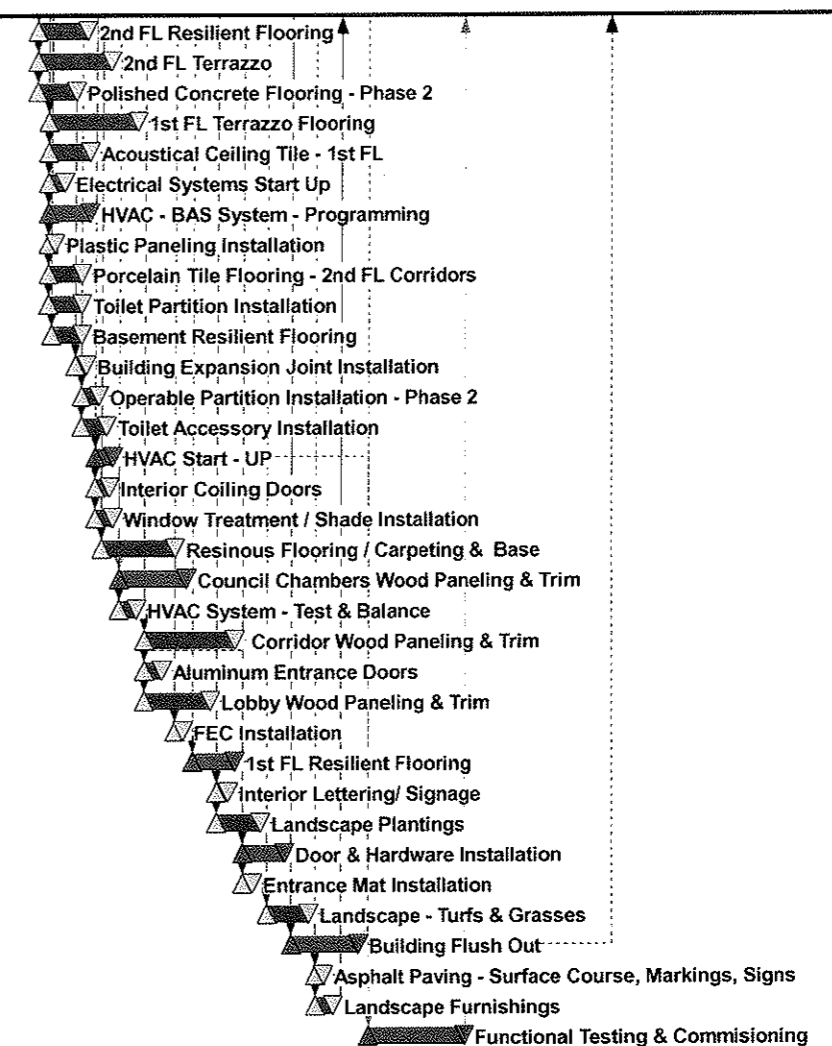

Project Start	08JAN18		Early Bar
Project Finish	16JUL19		Progress Bar
Data Date	06JUN18		Critical Activity
Run Date	06JUN18		

CMCP

